
### CITIES WITHOUT SLUMS

# Proposal Approval and Grant Set-Up Processing Time

Fiscal Years 2010 and 2011






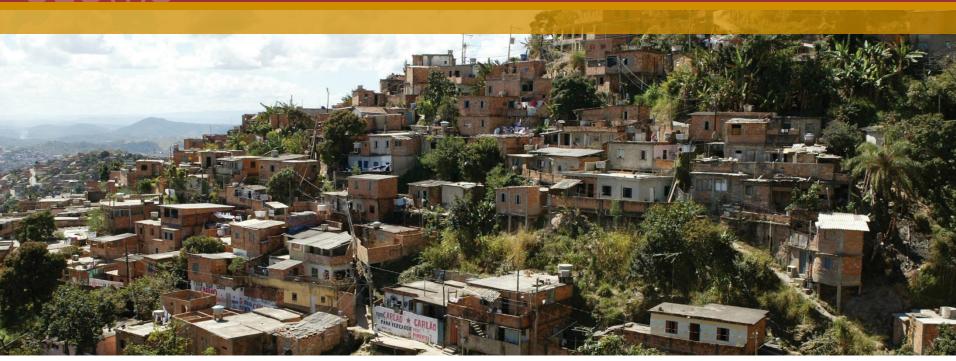



Average Proposal Approval Processing Time From Proposal Submission *to* Project Approval (Projects Approved in Fiscal Years 2010 and 2011)

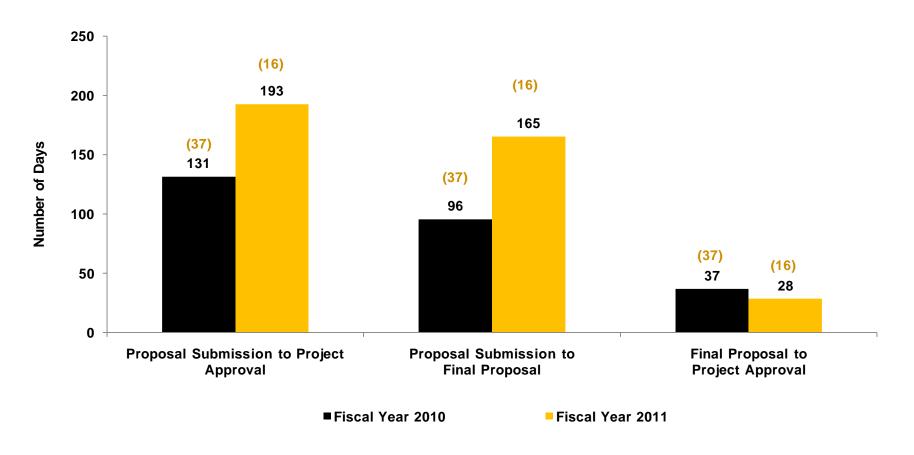





## Issues Contributing to Delays in Proposal Approval & Actions Taken/Recommended

#### Issues

- Delays in resubmission of revised proposals by applicant
- A large number of proposals received at the closure of old Grant Facility


### Action taken/ Recommendations

- Design of CATFund has eliminated the resubmission of proposals
- Processing of the 31<sup>st</sup> March batch is almost complete and this was a transition challenge not a permanent problem






## Overall Average Processing Time From Proposal Submission to Countersigned (Grant Agreements Countersigned in Fiscal Years 2010 and 2011)

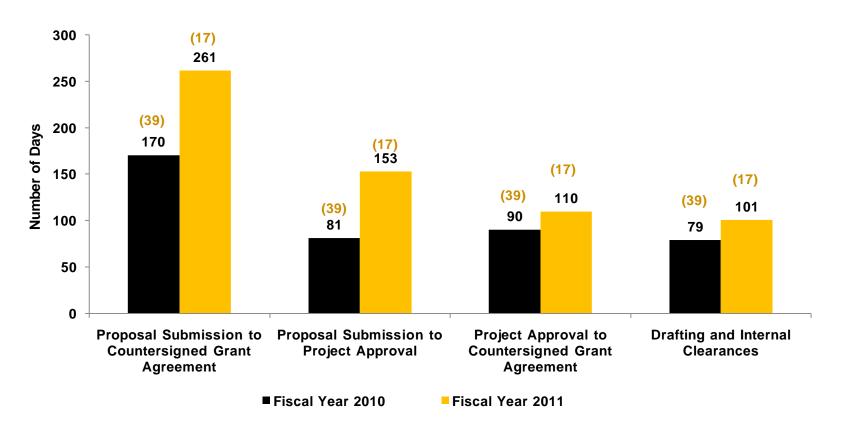






Average Grant Set Up Processing Time by *Grant Agreement Type*From Project Approval *to* Countersigned
(Grant Agreements Countersigned in Fiscal Years 2010 – 2011)

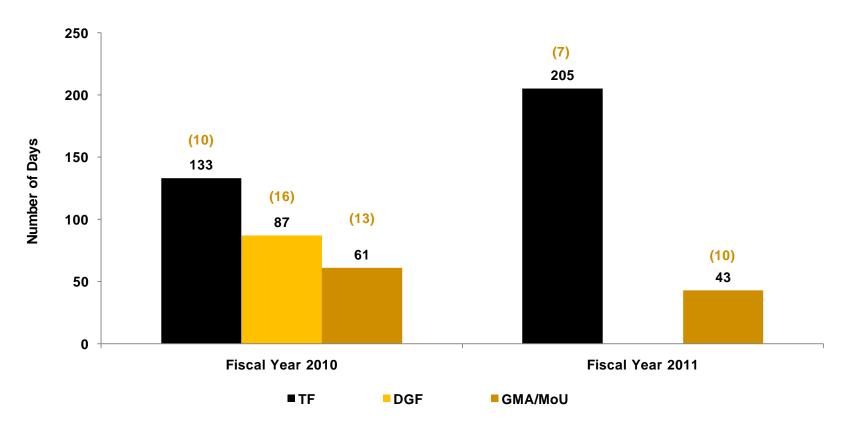





### Average Processing Time for Grant Agreement in Process From Project Approval to 28 February 2011

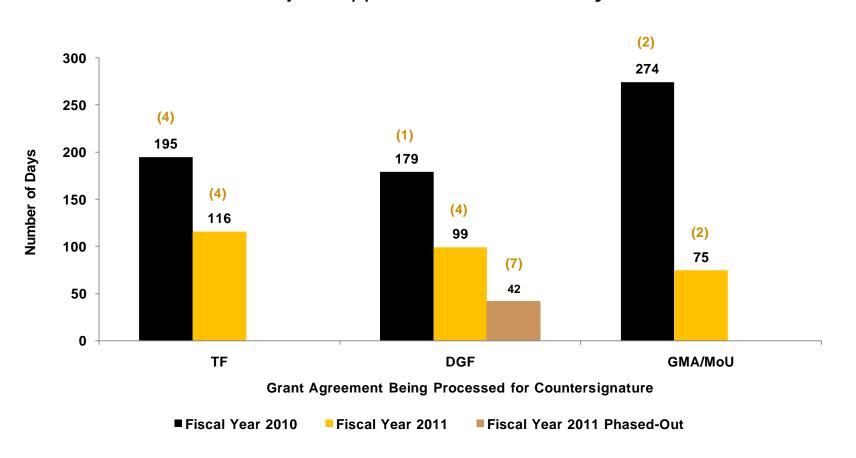





### Issues Contributing to Delays in Grant Set-up & Actions Taken/Recommended

#### Issues

- Enforcement of Country Director concurrence for all country specific projects
- Uncertainty about which Director should sign CA Trust Funded grant agreements

 Mandatory review by country Legal teams of all grant agreements for country specific projects

#### Actions Taken/Recommended

- Country Director concurrence already included in the design and processing of CATFund applications
- After various consultations with LEGOP, they reconfirmed the requirement of AMS 1.30 that all CA grant agreements for country specific projects are to be signed by Country Director
- Clear process and procedures for engaging country Legal teams including expected service standards (also for others e.g. Fiduciary/Safeguards)





### Issues Contributing to Delays in Grant Set-up & Actions Taken/Recommended

#### Issues

 Introduction of safeguards screening for all grants regardless of size

- Requirement that all grants to government ministries must be signed by Minister of Finance or equivalent
- Strengthened procurement procedures regardless of grant size

#### Actions Taken/Recommended

- Secretariat worked with Bank Safeguards team to develop tools
- Team members attended training and are carrying out the screening engaging Bank teams whenever needed
- Clear guidance and clarity on the accepted signatories from LEG
- Such requirements to be built into the application process for the CATFund
- CA has engaged a procurement specialist who assists the team in reviewing procurements aspects of proposals and provided clearance





## Average Grant Set-Up Processing Time by Grant Recipient Type (in days) From Project Approval to Receipt of Countersigned Grant Agreements (Countersigned in Fiscal Year 2011)

| Project<br>Approval<br>Fiscal Year | Project Title   | Country   | Assigned<br>Grant<br>Amount<br>(in US\$) | Grant Recipient   | Grant<br>Agreement<br>Type | Project Approval to<br>Countersigned Grant<br>Agreements | Drafting and<br>Internal<br>Clearances |
|------------------------------------|---|-----------|--|---|----------------------------|--|--|
| 2010                               | Indonesia Slum Alleviation Policy and<br>Action Plan (SAPOLA)   | Indonesia | 455,000                                  | Ministry of Finance   | TF                         | 245  | 235                                    |
| 2010                               | Jordan Secondary Cities Development<br>Strategy Program   | Jordan    | 476,000                                  | Ministry of Municipal<br>Affairs                                | TF                         | 126  | 107                                    |
| 2010                               | Namibian City Development Strategies (CDS) Pilot  | Namibia   | 250,000                                  | Association of Local<br>Authorities of<br>Namibia               | TF                         | 223  | 198                                    |
| 2009                               | Development of the National Urban<br>Policy and Strategic Urban<br>Development Plan for Uganda  | Uganda    | 450, 000                                 | Ministry of Lands,<br>Housing and Urban<br>Development          | TF                         | 471  | 425                                    |
| 2010                               | Shack/Slum Dwellers International: Transforming Settlements of the Urban Poor in Uganda: A Secondary Cities Support Programme (TSUPU) | Uganda    | 595,000                                  | Slum Dwellers<br>International                                  | TF                         | 211  | 205                                    |
| 2010                               | Strengthening Urban Local Governments in Uganda to Achieve the Goals of the TSUPU project   | Uganda    | 229,500                                  | International City<br>Management<br>Association                 | TF                         | 104  | 103                                    |
| 2010                               | Transforming the Settlements of the Urban Poor in Uganda A Secondary Cities Support Programme (TSUPU)                                 | Uganda    | 1,847,000                                | Ministry of Finance,<br>Planning and<br>Economic<br>Development | TF                         | 179  | 133                                    |





Thank you
